

ID	Task Name	Duration	Work	Start	Finish	Predecessors	Resource Names
1	<b>Foto XS - PR's</b>	<b>50 days</b>	<b>423 hrs</b>	<b>Mon 04/09/06</b>	<b>Mon 13/11/06</b>		
2	<b>Configuración y Desarrollo</b>	<b>47 days</b>	<b>326 hrs</b>	<b>Tue 05/09/06</b>	<b>Thu 09/11/06</b>		
3	PR 329	0,25 days	2 hrs	Tue 05/09/06	Tue 05/09/06		Gustavo
4	PR 87	0,25 days	2 hrs	Tue 05/09/06	Tue 05/09/06		Gustavo
5	PR 259	0,25 days	2 hrs	Tue 05/09/06	Tue 05/09/06		Gustavo
6	PR 276	0,25 days	2 hrs	Tue 05/09/06	Tue 05/09/06		Gustavo
7	PR 304	0,25 days	2 hrs	Wed 06/09/06	Wed 06/09/06		Gustavo
8	PR 337	0,5 days	4 hrs	Wed 06/09/06	Wed 06/09/06		Gustavo
9	PR 256	0,5 days	4 hrs	Wed 06/09/06	Wed 06/09/06		Gustavo
10	PR 22	0,25 days	2 hrs	Thu 07/09/06	Thu 07/09/06		Gustavo
11	PR 59	0,25 days	2 hrs	Thu 07/09/06	Thu 07/09/06		Gustavo
12	PR 5	0,25 days	2 hrs	Thu 07/09/06	Thu 07/09/06		Gustavo
13	PR 278	1 day	8 hrs	Fri 08/09/06	Fri 08/09/06		Gustavo
14	PR 240	0,5 days	4 hrs	Mon 11/09/06	Mon 11/09/06		Gustavo
15	PR 258	0,5 days	4 hrs	Mon 11/09/06	Mon 11/09/06		Gustavo
16	PR 268	0,75 days	6 hrs	Wed 13/09/06	Wed 13/09/06		Gustavo
17	PR 7	0,5 days	4 hrs	Thu 14/09/06	Thu 14/09/06		Gustavo
18	PR 89	0,5 days	4 hrs	Fri 15/09/06	Fri 15/09/06		Gustavo
19	PR 17	0,75 days	6 hrs	Mon 18/09/06	Mon 18/09/06		Gustavo
20	PR 372	8 days	16 hrs	Mon 18/09/06	Wed 27/09/06		Gustavo[25%]
21	PR 91 / 226	0,5 days	4 hrs	Tue 19/09/06	Tue 19/09/06		Gustavo
22	PR 241	0,5 days	4 hrs	Tue 19/09/06	Tue 19/09/06		Gustavo
23	PR 94	0,25 days	2 hrs	Tue 19/09/06	Tue 19/09/06		Gustavo
24	PR 280	0,25 days	2 hrs	Wed 20/09/06	Wed 20/09/06		Gustavo
25	PR 96	0,25 days	4 hrs	Wed 20/09/06	Wed 20/09/06		Gustavo,Mila
26	PR 103	1,5 days	12 hrs	Thu 21/09/06	Fri 22/09/06		Gustavo
27	PR 10	0,5 days	4 hrs	Fri 22/09/06	Fri 22/09/06		Gustavo
28	PR 193	0,25 days	2 hrs	Tue 26/09/06	Tue 26/09/06		Gustavo
29	<b>PR 3</b>	<b>5 days</b>	<b>40 hrs</b>	<b>Fri 29/09/06</b>	<b>Thu 05/10/06</b>		<b>Gustavo</b>
30	PR 117	2 days	8 hrs	Mon 09/10/06	Tue 10/10/06		Gustavo[50%]

Project: Plan PRs  
Date: Thu 21/09/06

Task Milestone External Tasks

Split Summary External Milestone

Progress Project Summary Deadline

ID	Task Name	Duration	Work	Start	Finish	Predecessors	Resource Names
31	PR 273	1 day	8 hrs	Wed 11/10/06	Wed 11/10/06	30	Gustavo
32	PR 132	1 day	8 hrs	Fri 13/10/06	Fri 13/10/06	31	Gustavo
33	PR 331	1 day	8 hrs	Mon 16/10/06	Mon 16/10/06	32	Gustavo
34	PR 62	1 day	8 hrs	Tue 17/10/06	Tue 17/10/06	33	Gustavo
35	PR 106	1 day	8 hrs	Wed 18/10/06	Wed 18/10/06	34	Gustavo
36	PR 102	1 day	8 hrs	Thu 19/10/06	Thu 19/10/06	35	Gustavo
37	PR 185	1 day	8 hrs	Fri 20/10/06	Fri 20/10/06	36	Gustavo
38	PR 14	1 day	8 hrs	Mon 23/10/06	Mon 23/10/06	37	Gustavo
39	PR 98	1 day	8 hrs	Tue 24/10/06	Tue 24/10/06	38	Gustavo
40	PR 90	1 day	8 hrs	Wed 25/10/06	Wed 25/10/06	39	Gustavo
41	PR 153	1 day	8 hrs	Thu 26/10/06	Thu 26/10/06	40	Gustavo
42	PR 15	1 day	8 hrs	Fri 27/10/06	Fri 27/10/06	41	Gustavo
43	PR 261	1 day	8 hrs	Mon 30/10/06	Mon 30/10/06	42	Gustavo
44	PR 8	1 day	8 hrs	Tue 31/10/06	Tue 31/10/06	43	Gustavo
45	PR 12	1 day	8 hrs	Wed 01/11/06	Wed 01/11/06	44	Gustavo
46	PR 18	1 day	8 hrs	Thu 02/11/06	Thu 02/11/06	45	Gustavo
47	PR 21	1 day	8 hrs	Fri 03/11/06	Fri 03/11/06	46	Gustavo
48	PR 175	1 day	8 hrs	Mon 06/11/06	Mon 06/11/06	47	Gustavo
49	PR 54	1 day	8 hrs	Tue 07/11/06	Tue 07/11/06	48	Gustavo
50	PR 377	1 day	8 hrs	Wed 08/11/06	Wed 08/11/06	49	Gustavo
51	PR 316	1 day	8 hrs	Thu 09/11/06	Thu 09/11/06	50	Gustavo
52	Ajustes recomendados	5 days	40 hrs	Mon 04/09/06	Fri 08/09/06		Gustavo
53	<b>Gerencia de Proyecto</b>	<b>45 days</b>	<b>57 hrs</b>	<b>Mon 11/09/06</b>	<b>Mon 13/11/06</b>		
54	Planificación	15 days	12 hrs	Tue 12/09/06	Mon 02/10/06		Listbeth[10%]
55	<b>Control y Seguimiento</b>	<b>42,5 days</b>	<b>21 hrs</b>	<b>Mon 11/09/06</b>	<b>Thu 09/11/06</b>		
56	11-09	0,5 days	3 hrs	Mon 11/09/06	Mon 11/09/06		Gustavo[25%];Kathy[25%];Listbeth[25%]
57	05-10	0,5 days	3 hrs	Thu 05/10/06	Thu 05/10/06		Gustavo[25%];Kathy[25%];Listbeth[25%]
58	11-10	0,5 days	3 hrs	Wed 11/10/06	Wed 11/10/06		Gustavo[25%];Kathy[25%];Listbeth[25%]
59	19-10	0,5 days	3 hrs	Thu 19/10/06	Thu 19/10/06		Gustavo[25%];Kathy[25%];Listbeth[25%]
60	26-10	0,5 days	3 hrs	Thu 26/10/06	Thu 26/10/06		Gustavo[25%];Kathy[25%];Listbeth[25%]

Project: Plan PRs  
Date: Thu 21/09/06

Task

Split

Progress

Milestone

Summary

Project Summary

External Tasks

External Milestone

Deadline

ID	Task Name	Duration	Work	Start	Finish	Predecessors	Resource Names
61	02-11	0,5 days	3 hrs	Thu 02/11/06	Thu 02/11/06		Gustavo[25%];Kathy[25%];Listbeth[25%]
62	09-11	0,5 days	3 hrs	Thu 09/11/06	Thu 09/11/06		Gustavo[25%];Kathy[25%];Listbeth[25%]
63	<b>Cierre</b>	<b>1 day</b>	<b>24 hrs</b>	<b>Mon 13/11/06</b>	<b>Mon 13/11/06</b>	<b>51</b>	<b>Gustavo;Kathy;Listbeth</b>

Project: Plan PRs  
Date: Thu 21/09/06

Task

Split

Progress

Milestone


Summary

Project Summary

External Tasks

External Milestone

Deadline

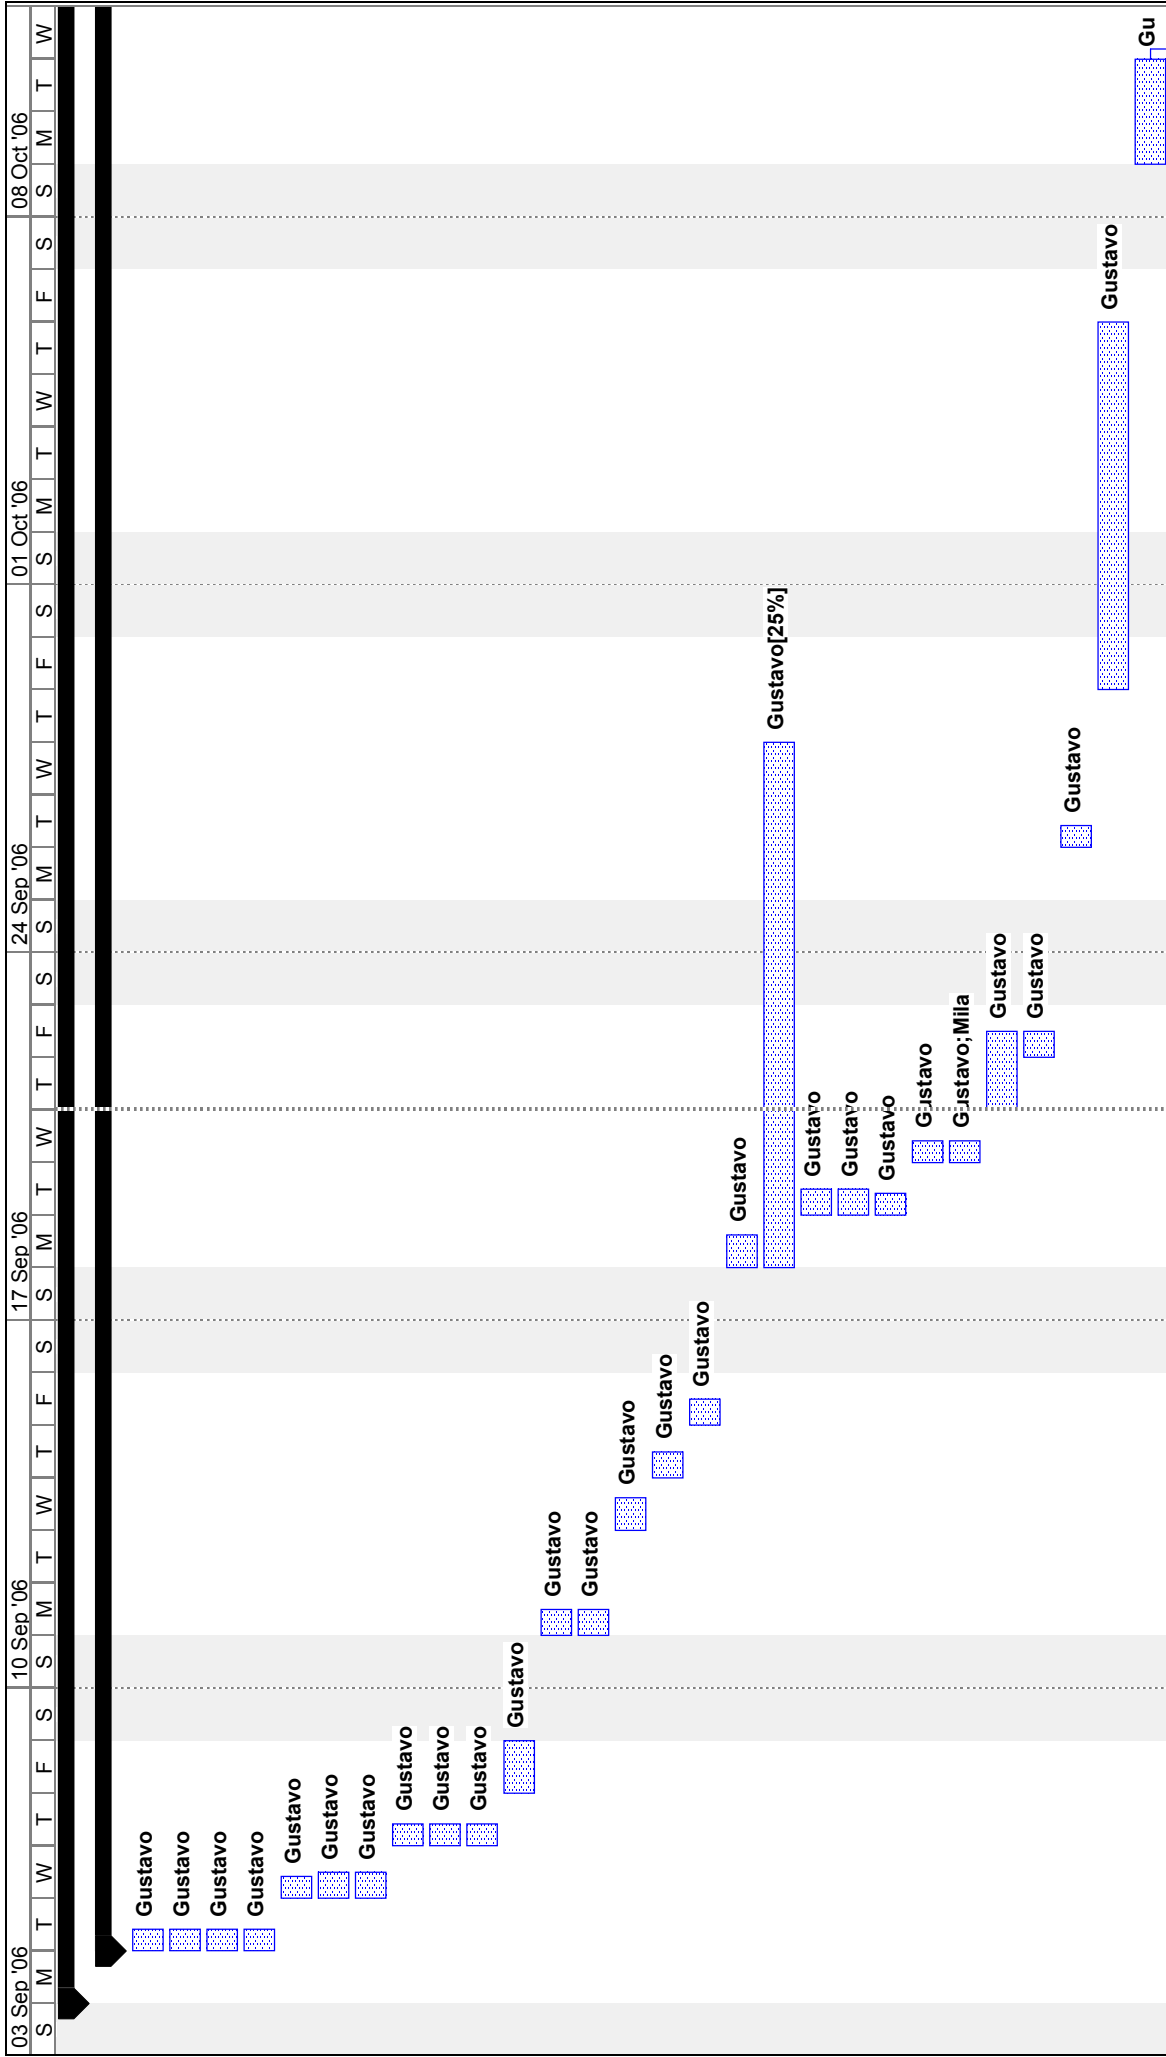


Project: Plan PRs  
Date: Thu 21/09/06

Task: Milestone: External Tasks:

Split: Summary: External Milestone:

Progress: Project Summary: Deadline:

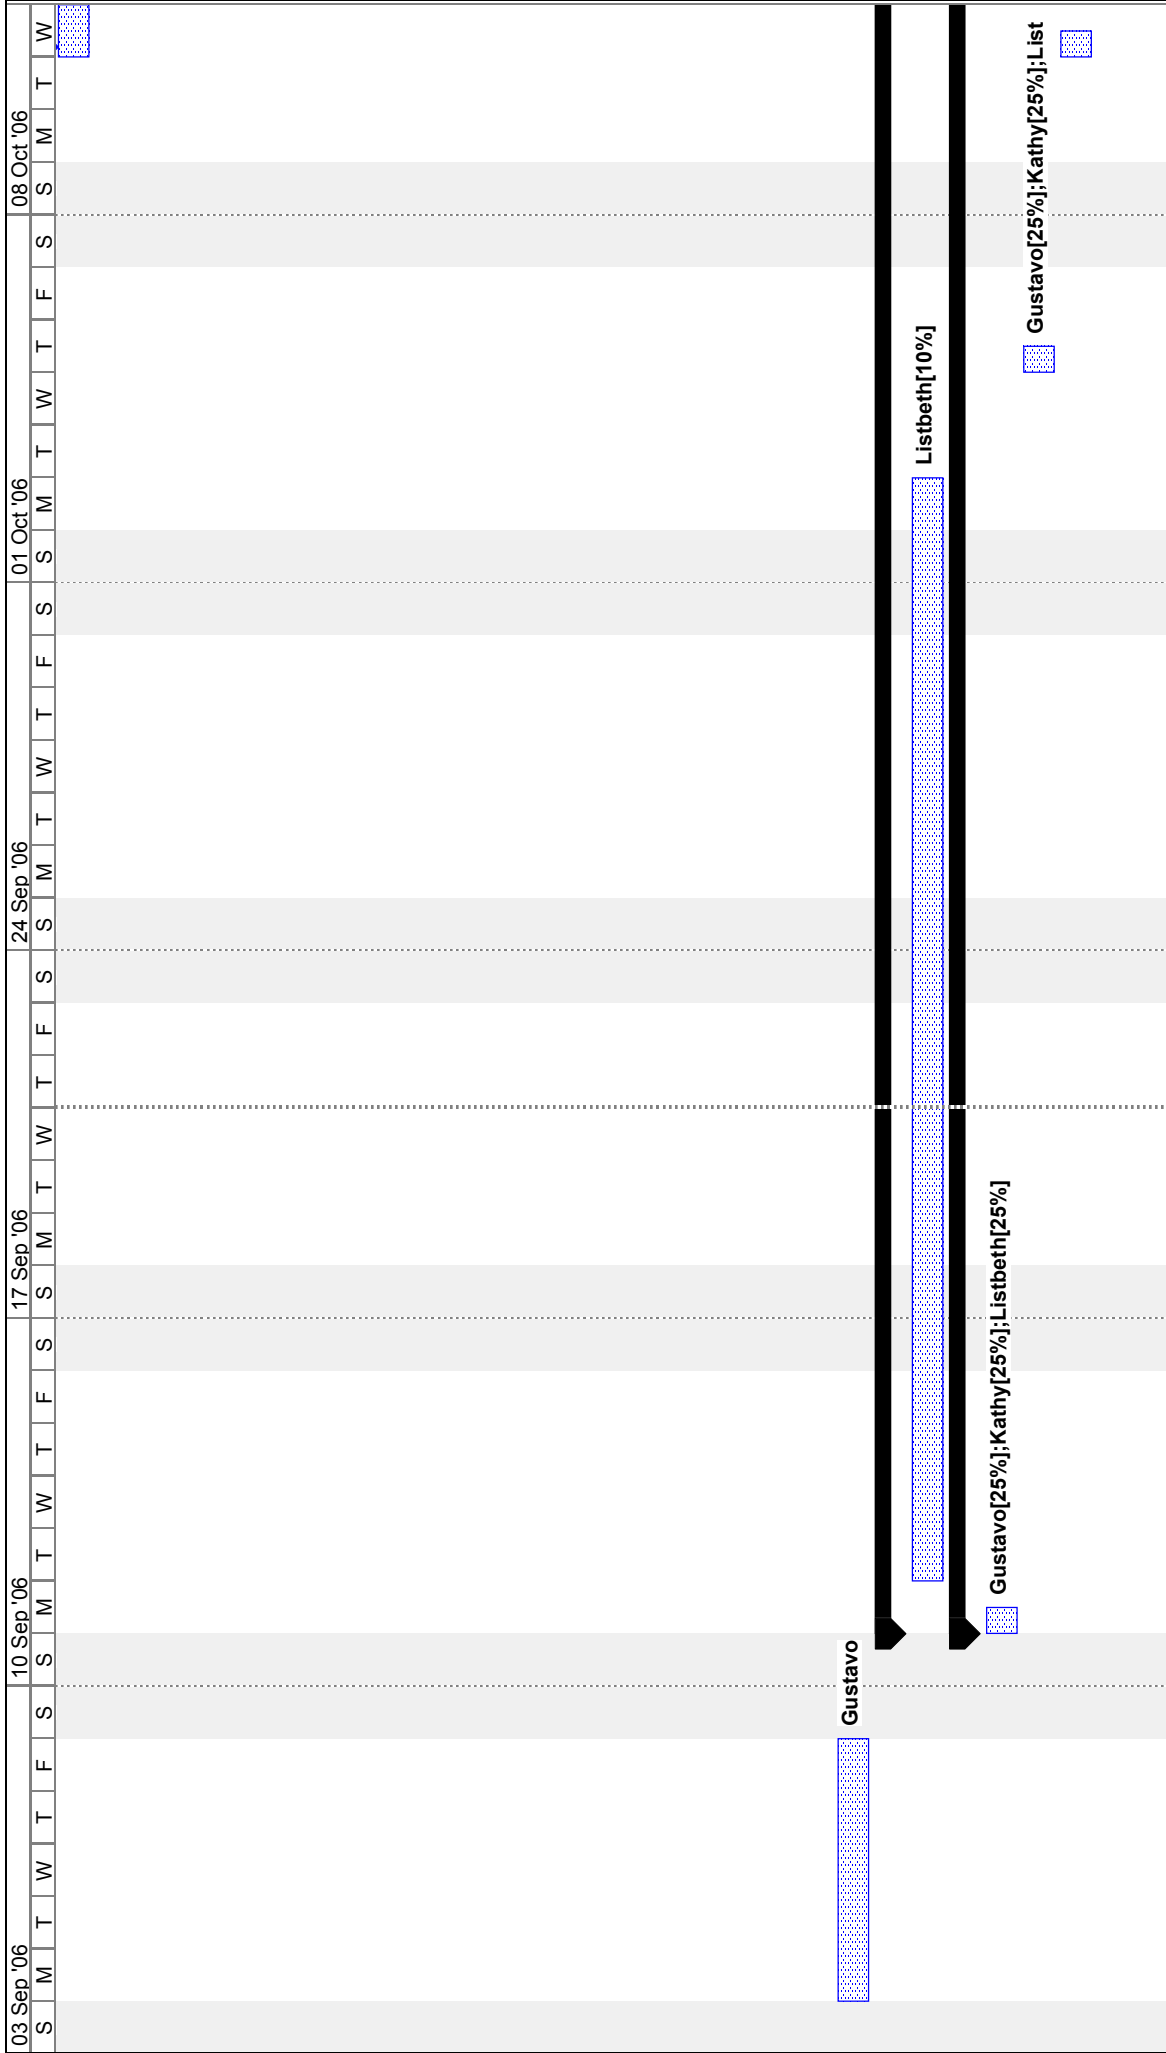

Project: Plan PRs  
Date: Thu 21/09/06

Task		Milestone	
Split		Summary	
Progress		Project Summary	
		External Tasks	
		External Milestone	
		Deadline	

03 Sep '06							10 Sep '06							17 Sep '06							24 Sep '06							01 Oct '06							08 Oct '06						
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S
[Shaded]							[Shaded]							[Shaded]							[Shaded]							[Shaded]													

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Project: Plan PRs  
Date: Thu 21/09/06



Project: Plan PRs  
 Date: Thu 21/09/06



