

ID	Task Name	Duration	Work	Start	Finish	% Complete	Predecessors	Resource Names	03 Sep '0
1	<b>Foto XS - PR's</b>	<b>50 days</b>	<b>424 hrs</b>	<b>Mon 04/09/06</b>	<b>Mon 13/11/06</b>	<b>20%</b>			S
2	<b>Configuración y Desarrollo</b>	<b>47 days</b>	<b>324 hrs</b>	<b>Tue 05/09/06</b>	<b>Thu 09/11/06</b>	<b>30%</b>			S
3	PR 329	0,25 days	2 hrs	Tue 05/09/06	Tue 05/09/06	100%		Gustavo	
4	PR 87	0,25 days	2 hrs	Tue 05/09/06	Tue 05/09/06	100%		Gustavo	
5	PR 259	0,25 days	2 hrs	Tue 05/09/06	Tue 05/09/06	100%		Gustavo	
6	PR 276	0,25 days	2 hrs	Tue 05/09/06	Tue 05/09/06	100%		Gustavo	
7	PR 304	0,25 days	2 hrs	Wed 06/09/06	Wed 06/09/06	100%		Gustavo	
8	PR 337	0,5 days	4 hrs	Wed 06/09/06	Wed 06/09/06	100%		Gustavo	
9	PR 256	0,5 days	4 hrs	Wed 06/09/06	Wed 06/09/06	100%		Gustavo	
10	PR 22	0,25 days	2 hrs	Thu 07/09/06	Thu 07/09/06	100%		Gustavo	
11	PR 59	0,25 days	2 hrs	Thu 07/09/06	Thu 07/09/06	100%		Gustavo	
12	PR 5	0,25 days	2 hrs	Thu 07/09/06	Thu 07/09/06	100%		Gustavo	
13	PR 278	1 day	8 hrs	Fri 08/09/06	Fri 08/09/06	100%		Gustavo	
14	PR 240	0,5 days	4 hrs	Mon 11/09/06	Mon 11/09/06	100%		Gustavo	
15	PR 258	0,5 days	4 hrs	Mon 11/09/06	Mon 11/09/06	100%		Gustavo	
16	PR 268	0,75 days	6 hrs	Wed 13/09/06	Wed 13/09/06	100%		Gustavo	
17	PR 7	0,5 days	4 hrs	Thu 14/09/06	Thu 14/09/06	100%		Gustavo	
18	PR 89	0,5 days	4 hrs	Fri 15/09/06	Fri 15/09/06	100%		Gustavo	
19	PR 17	0,75 days	6 hrs	Mon 18/09/06	Mon 18/09/06	100%		Gustavo	
20	PR 372	8 days	16 hrs	Mon 18/09/06	Wed 27/09/06	50%		Gustavo[25%]	
21	PR 91 / 226	0,5 days	4 hrs	Tue 19/09/06	Tue 19/09/06	90%		Gustavo	
22	PR 241	2,5 days	2 hrs	Tue 19/09/06	Thu 21/09/06	80%		Gustavo[10%]	
23	PR 94	0,25 days	2 hrs	Tue 19/09/06	Tue 19/09/06	100%		Gustavo	
24	PR 280	0,25 days	2 hrs	Wed 20/09/06	Wed 20/09/06	100%		Gustavo	
25	PR 96	0,25 days	4 hrs	Wed 20/09/06	Wed 20/09/06	100%		Gustavo,Mila	
26	PR 103	1,5 days	12 hrs	Thu 21/09/06	Fri 22/09/06	0%		Gustavo	
27	PR 10	0,5 days	4 hrs	Fri 22/09/06	Fri 22/09/06	0%		Gustavo	
28	PR 193	0,25 days	2 hrs	Tue 26/09/06	Tue 26/09/06	0%		Gustavo	
29	<b>PR 3</b>	<b>5 days</b>	<b>40 hrs</b>	<b>Fri 29/09/06</b>	<b>Thu 05/10/06</b>	<b>0%</b>		<b>Gustavo</b>	
30	PR 117	2 days	8 hrs	Mon 09/10/06	Tue 10/10/06	0%		Gustavo[50%]	

Project: Plan PRs  
Date: Thu 21/09/06

Task

Split

Progress

Milestone

Summary

Project Summary

External Tasks

External Milestone

Deadline

ID	Task Name	Duration	Work	Start	Finish	% Complete	Predecessors	Resource Names	03 Sep '0		
									S	S	M
31	PR 273	1 day	8 hrs	Wed 11/10/06	Wed 11/10/06	0%	30	Gustavo			
32	PR 132	1 day	8 hrs	Fri 13/10/06	Fri 13/10/06	0%	31	Gustavo			
33	PR 331	1 day	8 hrs	Mon 16/10/06	Mon 16/10/06	0%	32	Gustavo			
34	PR 62	1 day	8 hrs	Tue 17/10/06	Tue 17/10/06	0%	33	Gustavo			
35	PR 106	1 day	8 hrs	Wed 18/10/06	Wed 18/10/06	0%	34	Gustavo			
36	PR 102	1 day	8 hrs	Thu 19/10/06	Thu 19/10/06	0%	35	Gustavo			
37	PR 185	1 day	8 hrs	Fri 20/10/06	Fri 20/10/06	0%	36	Gustavo			
38	PR 14	1 day	8 hrs	Mon 23/10/06	Mon 23/10/06	0%	37	Gustavo			
39	PR 98	1 day	8 hrs	Tue 24/10/06	Tue 24/10/06	0%	38	Gustavo			
40	PR 90	1 day	8 hrs	Wed 25/10/06	Wed 25/10/06	0%	39	Gustavo			
41	PR 153	1 day	8 hrs	Thu 26/10/06	Thu 26/10/06	0%	40	Gustavo			
42	PR 15	1 day	8 hrs	Fri 27/10/06	Fri 27/10/06	0%	41	Gustavo			
43	PR 261	1 day	8 hrs	Mon 30/10/06	Mon 30/10/06	0%	42	Gustavo			
44	PR 8	1 day	8 hrs	Tue 31/10/06	Tue 31/10/06	0%	43	Gustavo			
45	PR 12	1 day	8 hrs	Wed 01/11/06	Wed 01/11/06	0%	44	Gustavo			
46	PR 18	1 day	8 hrs	Thu 02/11/06	Thu 02/11/06	0%	45	Gustavo			
47	PR 21	1 day	8 hrs	Fri 03/11/06	Fri 03/11/06	0%	46	Gustavo			
48	PR 175	1 day	8 hrs	Mon 06/11/06	Mon 06/11/06	0%	47	Gustavo			
49	PR 54	1 day	8 hrs	Tue 07/11/06	Tue 07/11/06	0%	48	Gustavo			
50	PR 377	1 day	8 hrs	Wed 08/11/06	Wed 08/11/06	0%	49	Gustavo			
51	PR 316	1 day	8 hrs	Thu 09/11/06	Thu 09/11/06	0%	50				
52	Ajustes recomendados	5 days	40 hrs	Mon 04/09/06	Fri 08/09/06	0%		Gustavo			
53	<b>Gerencia de Proyecto</b>	<b>45 days</b>	<b>60 hrs</b>	<b>Mon 11/09/06</b>	<b>Mon 13/11/06</b>	<b>0%</b>					
54	Planificación	15 days	12 hrs	Tue 12/09/06	Mon 02/10/06	0%		Listbeth[10%]			
55	<b>Control y Seguimiento</b>	<b>34,5 days</b>	<b>24 hrs</b>	<b>Mon 11/09/06</b>	<b>Mon 30/10/06</b>	<b>0%</b>					
56	11-09	0,5 days	3 hrs	Mon 11/09/06	Mon 11/09/06	0%		Gustavo[25%];Kathy[2			
57	18-09	0,5 days	3 hrs	Mon 18/09/06	Mon 18/09/06	0%		Gustavo[25%];Kathy[2			
58	25-09	0,5 days	3 hrs	Mon 25/09/06	Mon 25/09/06	0%		Gustavo[25%];Kathy[2			
59	02-10	0,5 days	3 hrs	Mon 02/10/06	Mon 02/10/06	0%		Gustavo[25%];Kathy[2			
60	09-10	0,5 days	3 hrs	Mon 09/10/06	Mon 09/10/06	0%		Gustavo[25%];Kathy[2			

Project: Plan PRs  
Date: Thu 21/09/06

Task

Split

Progress

Milestone

Summary


Project Summary

External Tasks


External Milestone

Deadline


ID	Task Name	Duration	Work	Start	Finish	% Complete	Predecessors	Resource Names	03 Sep '0		
									S	S	M
61	16-10	0.5 days	3 hrs	Mon 16/10/06	Mon 16/10/06	0%		Gustavo[25%];Kathy[2			
62	23-10	0.5 days	3 hrs	Mon 23/10/06	Mon 23/10/06	0%		Gustavo[25%];Kathy[2			
63	30-10	0.5 days	3 hrs	Mon 30/10/06	Mon 30/10/06	0%		Gustavo[25%];Kathy[2			
64	<b>Cierre</b>	<b>1 day</b>	<b>24 hrs</b>	<b>Mon 13/11/06</b>	<b>Mon 13/11/06</b>	<b>0%</b>	<b>51</b>	<b>Gustavo;Kathy;Listb</b>			



Project: Plan PRs  
Date: Thu 21/09/06

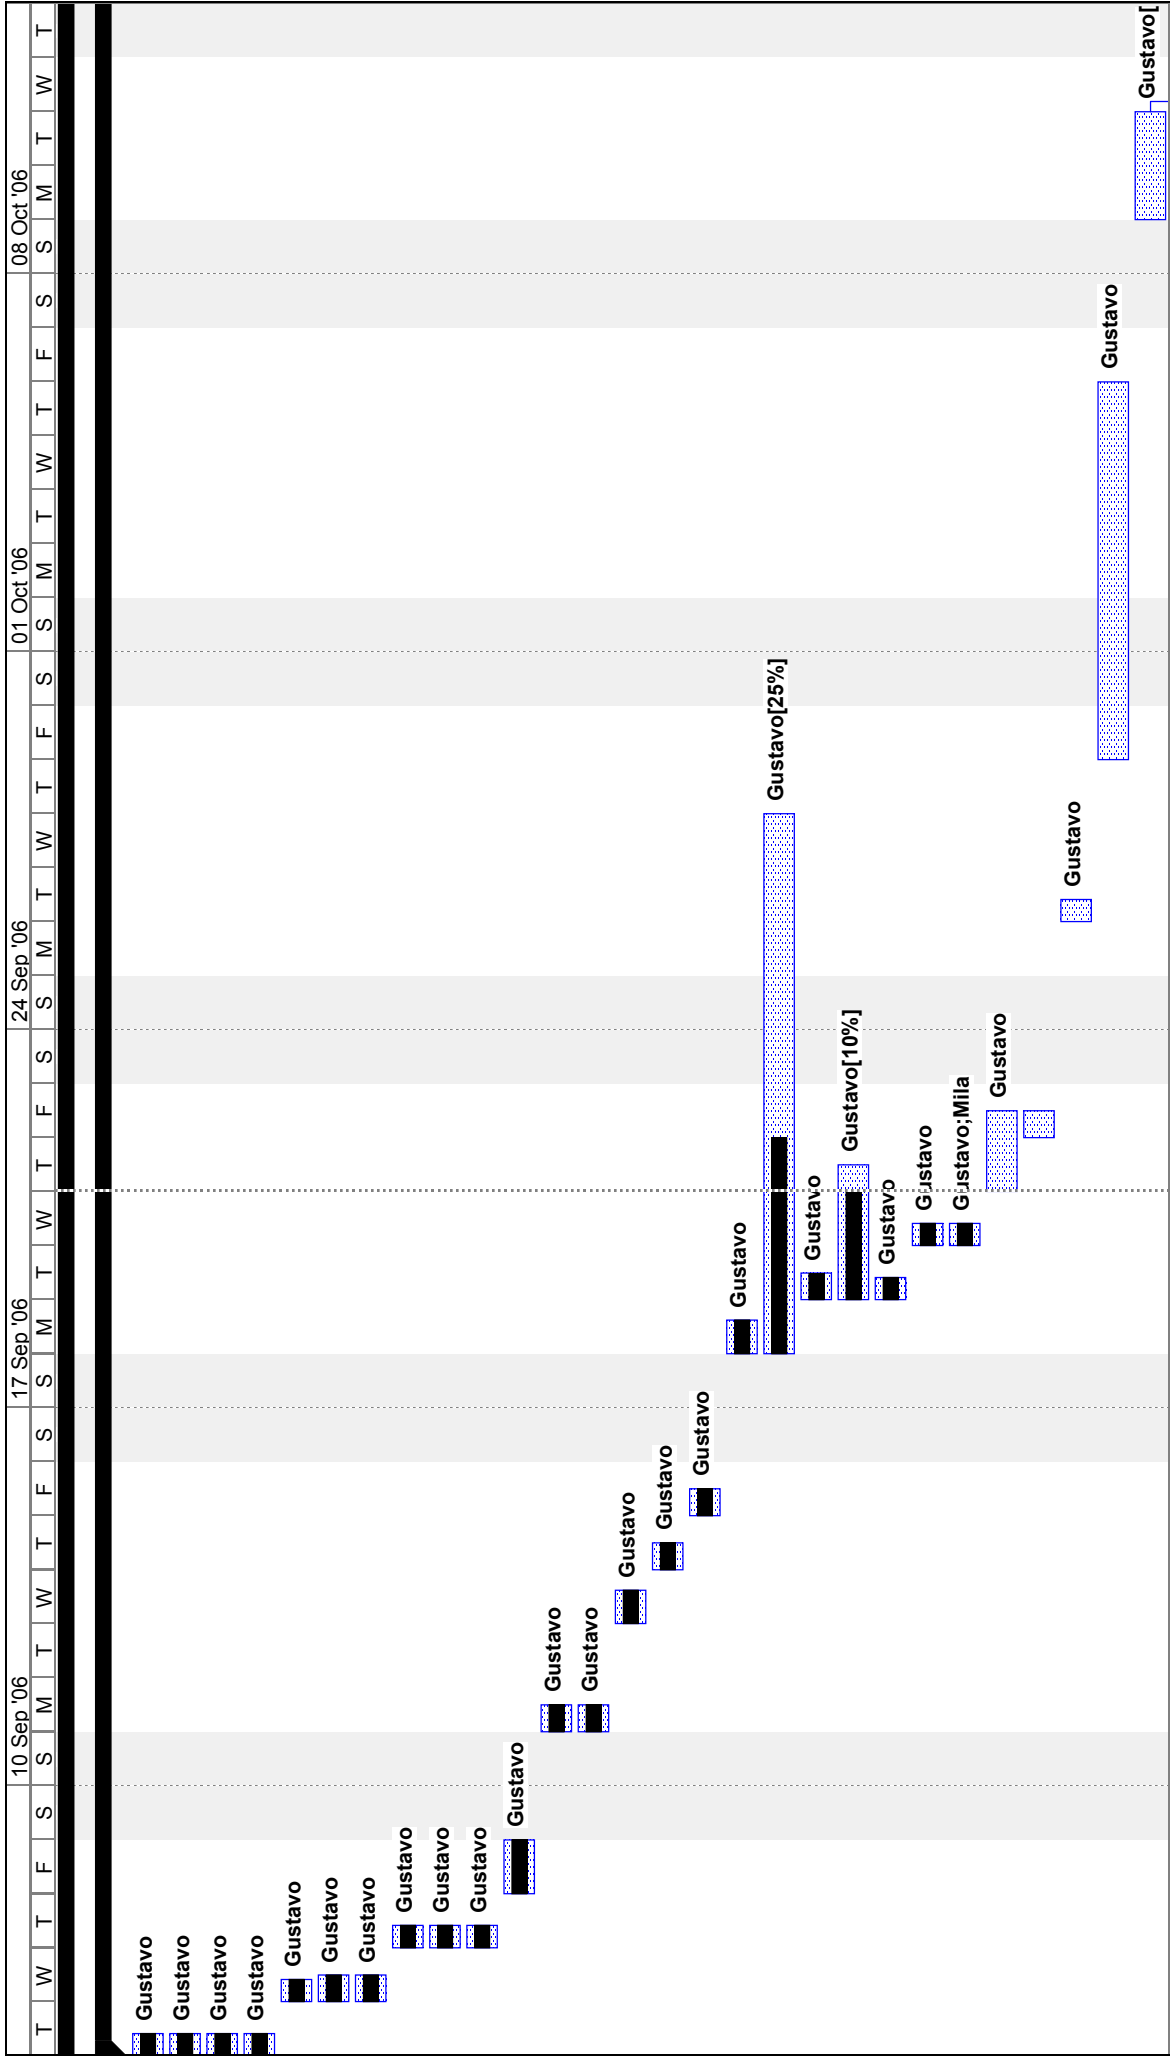

Project: Plan PRs  
Date: Thu 21/09/06

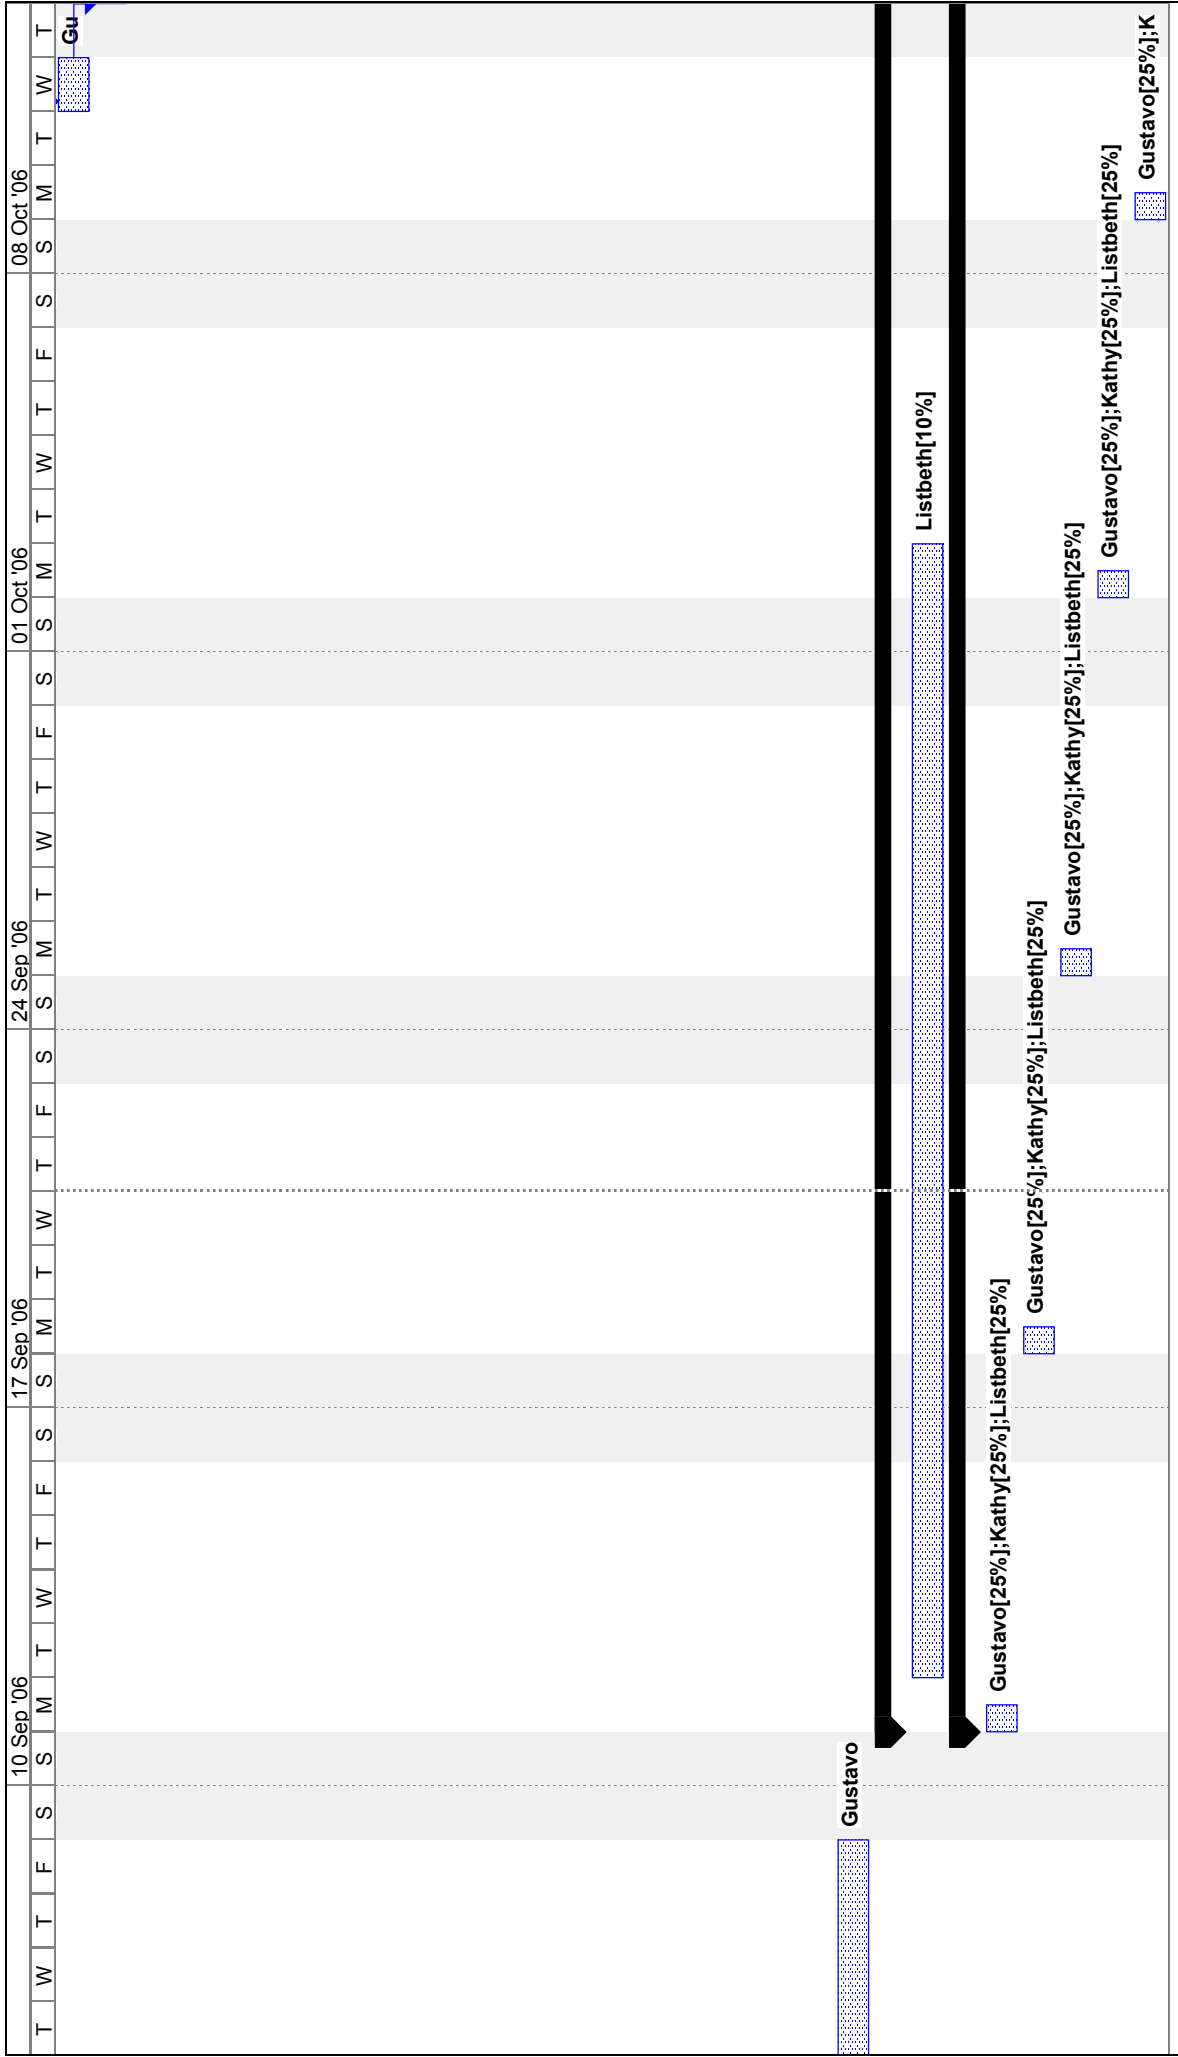



Project: Plan PRs  
Date: Thu 21/09/06


Task		External Tasks	
Split		Milestone	
Progress		Summary	
		Project Summary	
		External Milestone	
		Deadline	


10 Sep '06			17 Sep '06			24 Sep '06			01 Oct '06			08 Oct '06															
T	W	T	F	S	S	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T					


Project: Plan PRs  
Date: Thu 21/09/06


Task 


Split 


Progress 


Milestone 

Summary 


Project Summary 

External Tasks 

External Milestone 

Deadline 



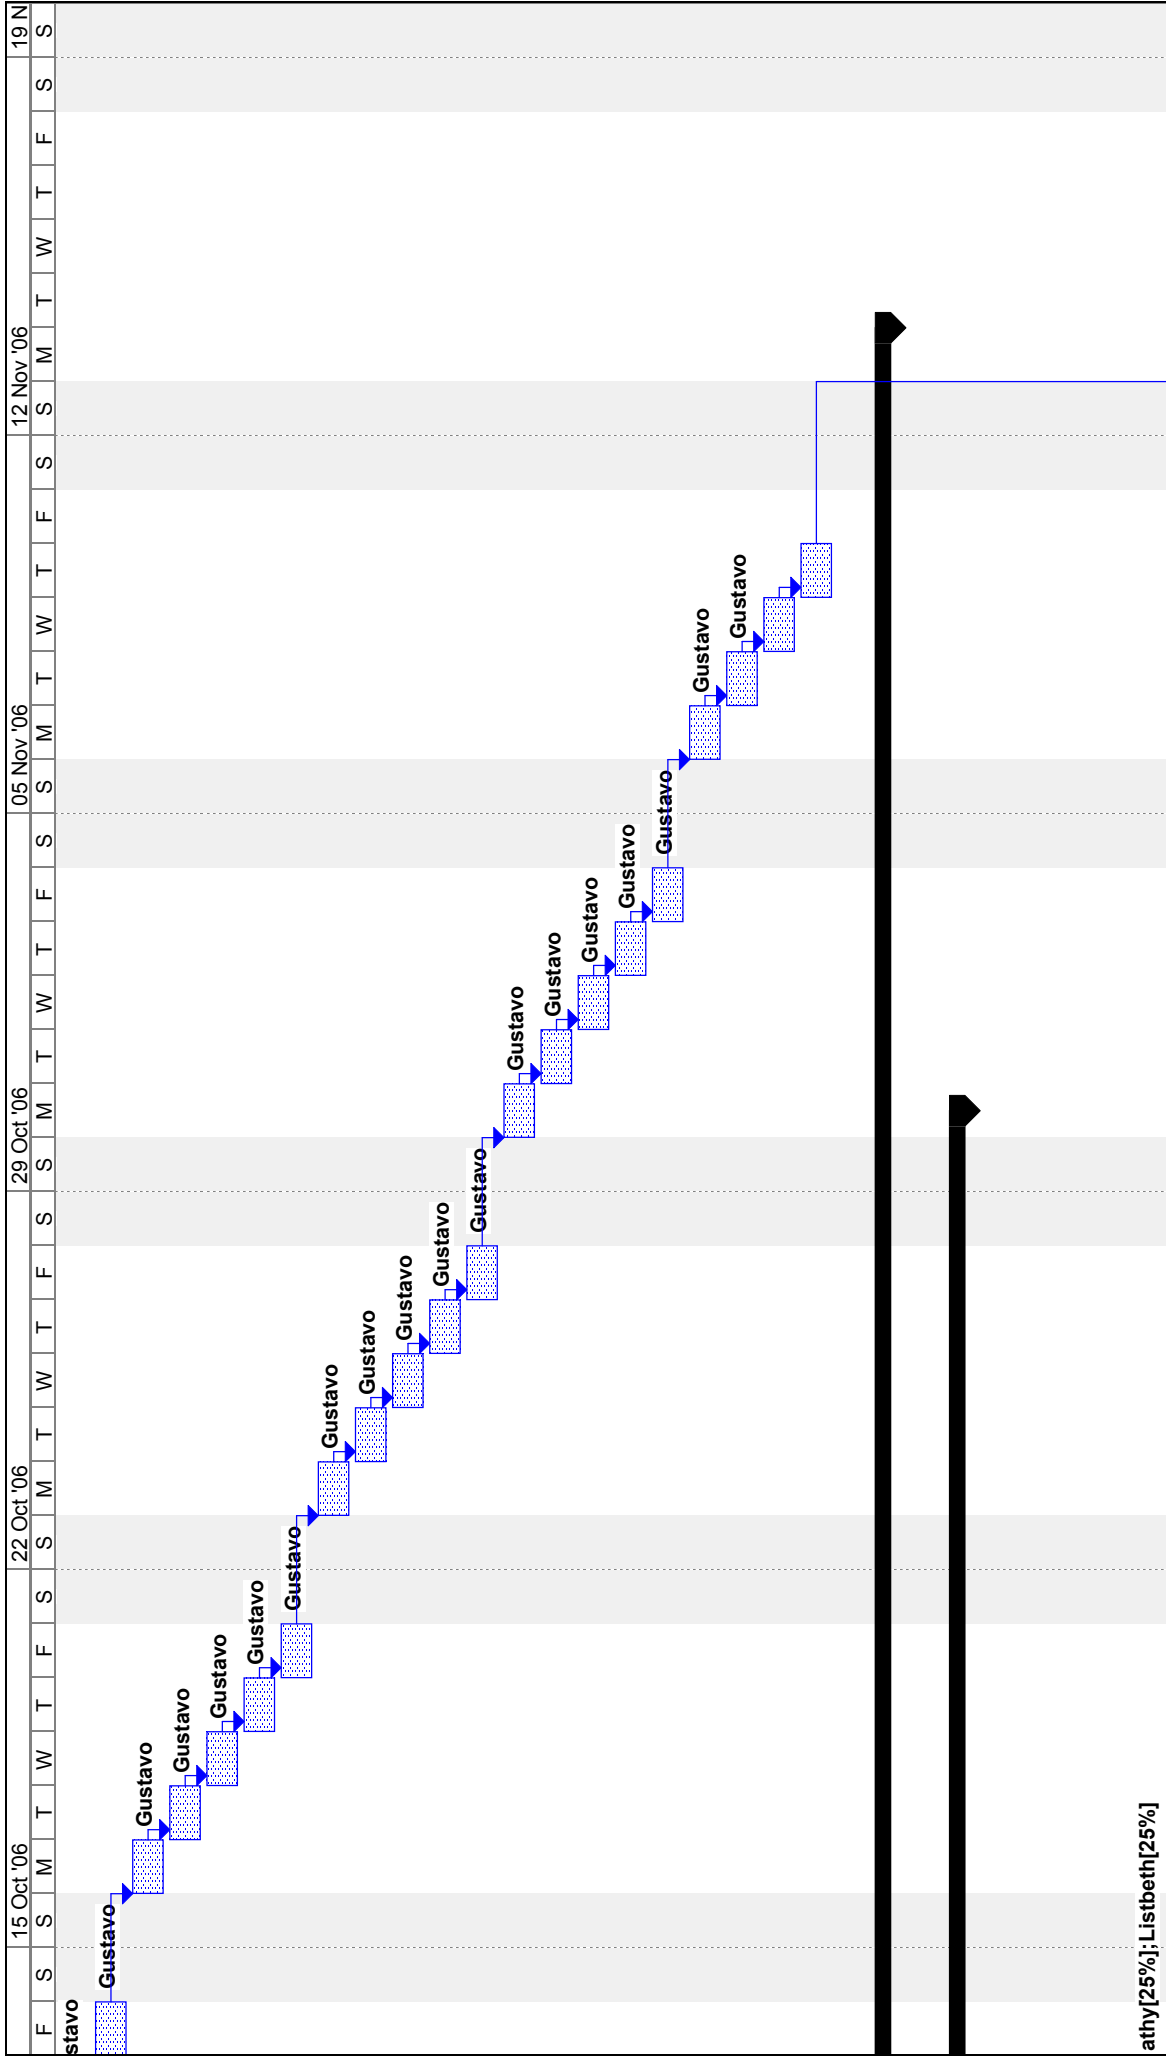

athy[25%];Listbeth[25%]

Project: Plan PRs Date: Thu 21/09/06	<ul style="list-style-type: none"> <li>Task</li> <li>Milestone</li> <li>Summary</li> <li>Project Summary</li> </ul>	<ul style="list-style-type: none"> <li>External Tasks</li> <li>External Milestone</li> <li>Deadline</li> </ul>
---	---	--

