











ID	Task Name	Duration	Work	Start	Finish	% Complete	03 Sep '06							10 S
							S	M	T	W	T	F	S	
1	Foto XS - PR's	49 days	356 hrs	Tue 05/09/06	Mon 13/11/06	51%								
2	Configuración y Desarrollo	43 days	256 hrs	Tue 05/09/06	Fri 03/11/06	87%								
3	PR 329	0,25 days	2 hrs	Tue 05/09/06	Tue 05/09/06	100%								
4	PR 87	0,25 days	2 hrs	Tue 05/09/06	Tue 05/09/06	100%								
5	PR 259	0,25 days	2 hrs	Tue 05/09/06	Tue 05/09/06	100%								
6	PR 276	0,25 days	2 hrs	Tue 05/09/06	Tue 05/09/06	100%								
7	PR 304	0,25 days	2 hrs	Wed 06/09/06	Wed 06/09/06	100%								
8	PR 337	0,5 days	4 hrs	Wed 06/09/06	Wed 06/09/06	100%								
9	PR 256	0,5 days	4 hrs	Wed 06/09/06	Wed 06/09/06	100%								
10	PR 22	0,25 days	2 hrs	Thu 07/09/06	Thu 07/09/06	100%								
11	PR 59	0,25 days	2 hrs	Thu 07/09/06	Thu 07/09/06	100%								
12	PR 5	0,25 days	2 hrs	Thu 07/09/06	Thu 07/09/06	100%								
13	PR 278	1 day	8 hrs	Fri 08/09/06	Fri 08/09/06	100%								
14	PR 240	0,5 days	4 hrs	Mon 11/09/06	Mon 11/09/06	100%								
15	PR 258	0,5 days	4 hrs	Mon 11/09/06	Mon 11/09/06	100%								
16	PR 268	0,75 days	6 hrs	Wed 13/09/06	Wed 13/09/06	100%								
17	PR 7	0,5 days	4 hrs	Thu 14/09/06	Thu 14/09/06	100%								
18	PR 89	0,5 days	4 hrs	Fri 15/09/06	Fri 15/09/06	100%								
19	PR 17	0,75 days	6 hrs	Mon 18/09/06	Mon 18/09/06	100%								
20	PR 372	8 days	16 hrs	Mon 18/09/06	Wed 27/09/06	100%								
21	PR 94	0,25 days	2 hrs	Tue 19/09/06	Tue 19/09/06	100%								
22	PR 280	0,25 days	2 hrs	Wed 20/09/06	Wed 20/09/06	100%								
23	PR 96	0,25 days	4 hrs	Wed 20/09/06	Wed 20/09/06	100%								
24	PR 103	1,5 days	12 hrs	Thu 21/09/06	Fri 22/09/06	100%								
25	PR 10	0,5 days	4 hrs	Fri 22/09/06	Fri 22/09/06	100%								
26	PR 193	0,25 days	2 hrs	Tue 26/09/06	Tue 26/09/06	100%								
27	PR 117	2 days	8 hrs	Mon 09/10/06	Tue 10/10/06	100%								
28	PR 273	1 day	8 hrs	Wed 11/10/06	Wed 11/10/06	100%								
29	PR 102	1 day	8 hrs	Tue 17/10/06	Tue 17/10/06	100%								
30	PR 185	1 day	8 hrs	Wed 18/10/06	Wed 18/10/06	100%								
31	PR 14	1 day	8 hrs	Thu 19/10/06	Thu 19/10/06	100%								

Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo
 Gustavo


Project: Plan PRs Date: Wed 01/11/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Work	Start	Finish	% Complete	03 Sep '06							10 S
							S	M	T	W	T	F	S	S
32	PR 21	1 day	8 hrs	Wed 01/11/06	Wed 01/11/06	100%								
33	PR 170	1 day	8 hrs	Tue 24/10/06	Tue 24/10/06	100%								
34	PR 18	1 day	8 hrs	Thu 26/10/06	Fri 27/10/06	100%								
35	PR 241	2,5 days	2 hrs	Tue 19/09/06	Fri 27/10/06	100%								
36	PR 93	1 day	8 hrs	Wed 25/10/06	Mon 30/10/06	50%								
37	PR 3	5 days	80 hrs	Mon 30/10/06	Fri 03/11/06	15%								
38	Ajustes recomendados	5 days	40 hrs	Mon 06/11/06	Fri 10/11/06	0%								
39	Gerencia de Proyecto	45 days	60 hrs	Mon 11/09/06	Mon 13/11/06	0%								
40	Planificación	15 days	12 hrs	Tue 12/09/06	Mon 02/10/06	0%								
41	Control y Seguimiento	34,5 days	24 hrs	Mon 11/09/06	Mon 30/10/06	0%								
42	11-09	0,5 days	3 hrs	Mon 11/09/06	Mon 11/09/06	0%								
43	18-09	0,5 days	3 hrs	Mon 18/09/06	Mon 18/09/06	0%								
44	25-09	0,5 days	3 hrs	Mon 25/09/06	Mon 25/09/06	0%								
45	02-10	0,5 days	3 hrs	Mon 02/10/06	Mon 02/10/06	0%								
46	09-10	0,5 days	3 hrs	Mon 09/10/06	Mon 09/10/06	0%								
47	16-10	0,5 days	3 hrs	Mon 16/10/06	Mon 16/10/06	0%								
48	23-10	0,5 days	3 hrs	Mon 23/10/06	Mon 23/10/06	0%								
49	30-10	0,5 days	3 hrs	Mon 30/10/06	Mon 30/10/06	0%								
50	Cierre	1 day	24 hrs	Mon 13/11/06	Mon 13/11/06	0%								


Project: Plan PRs Date: Wed 01/11/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

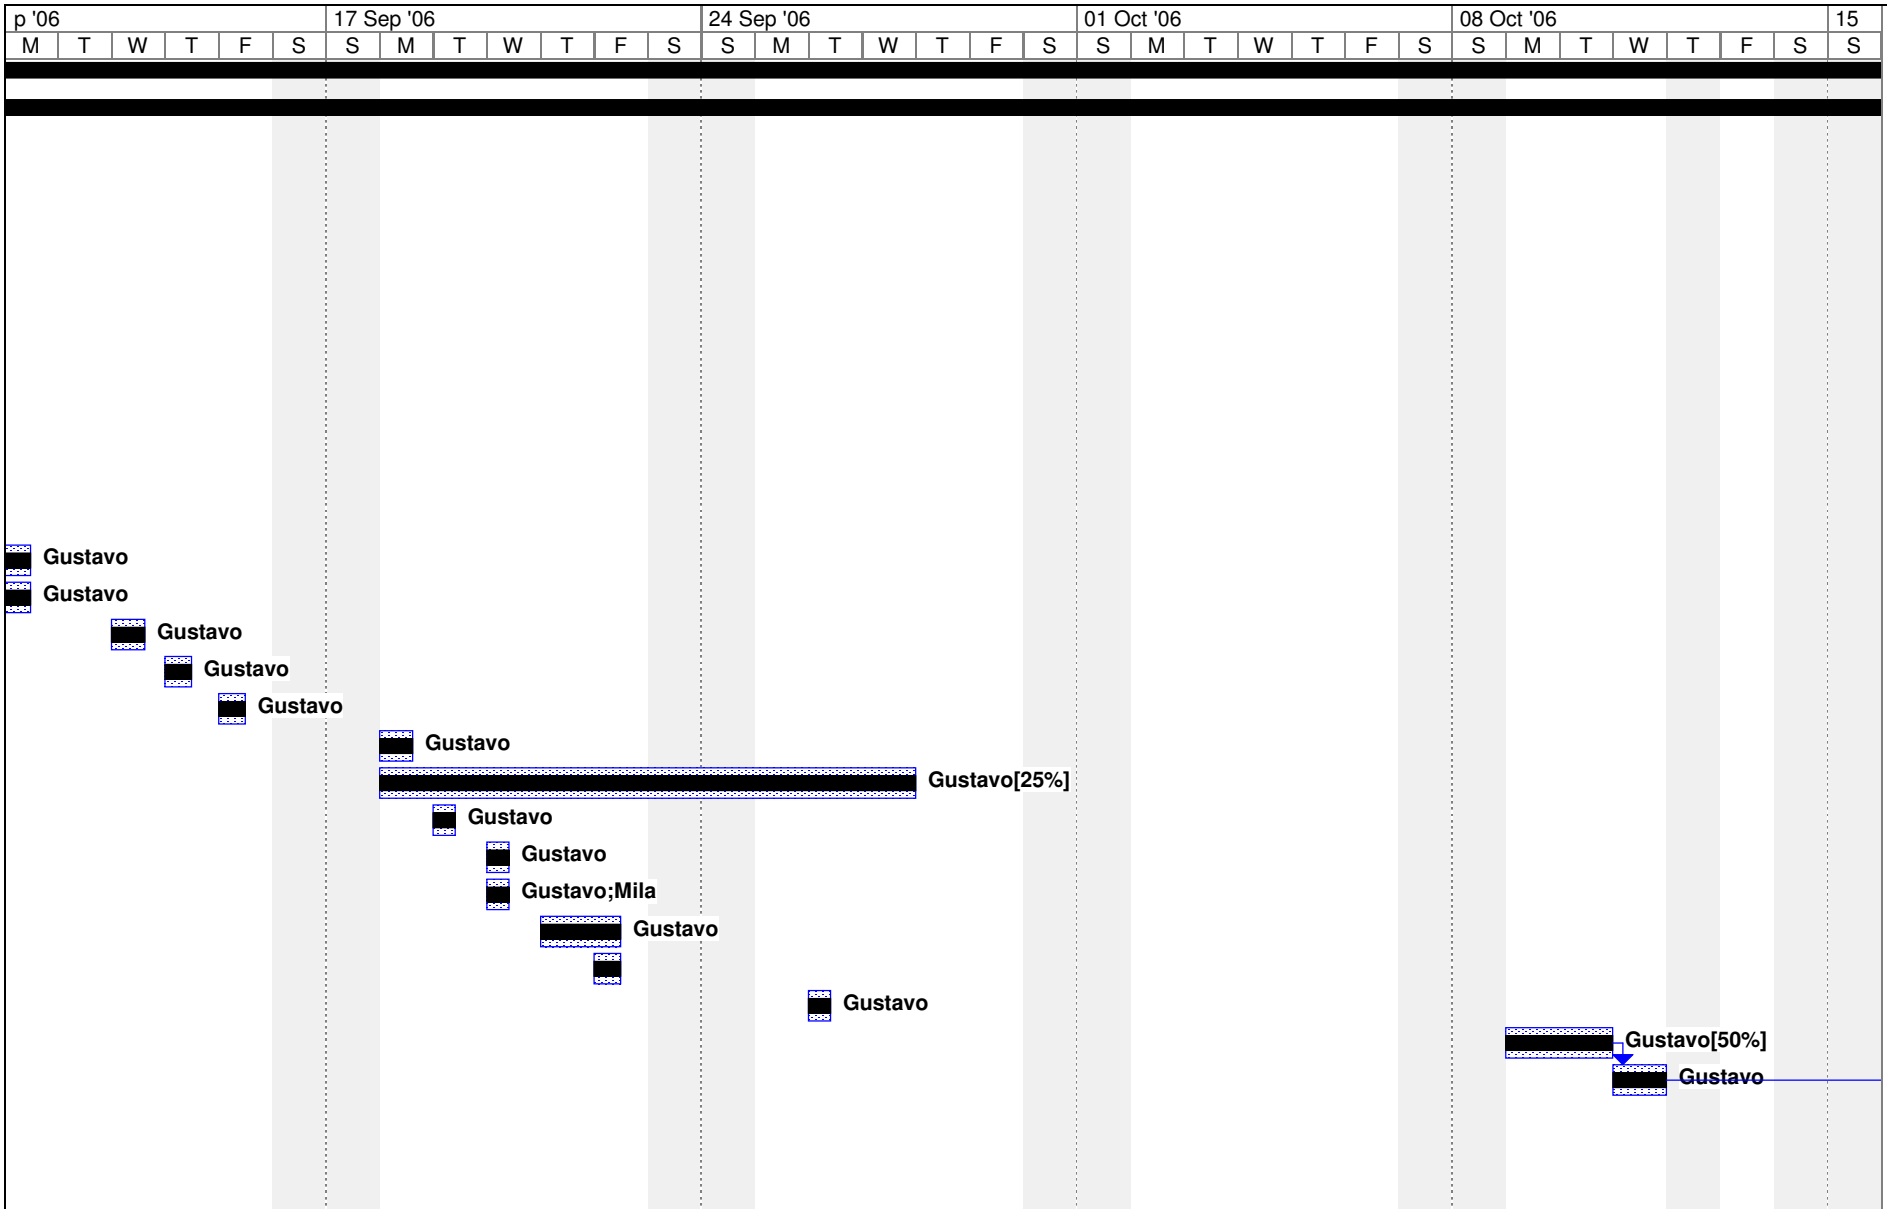




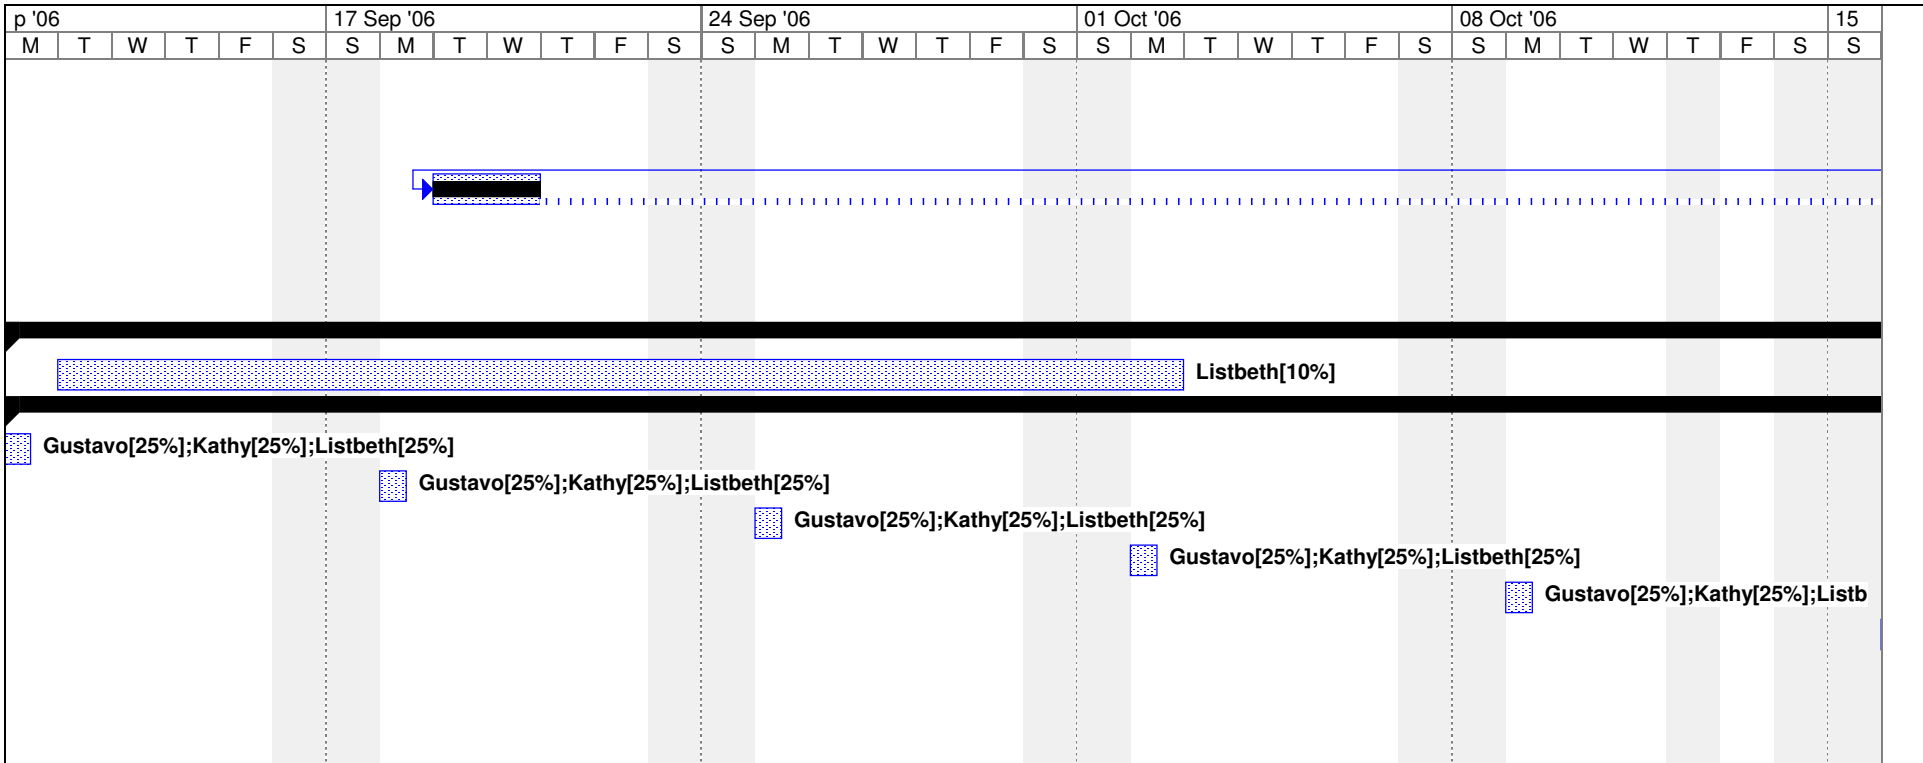



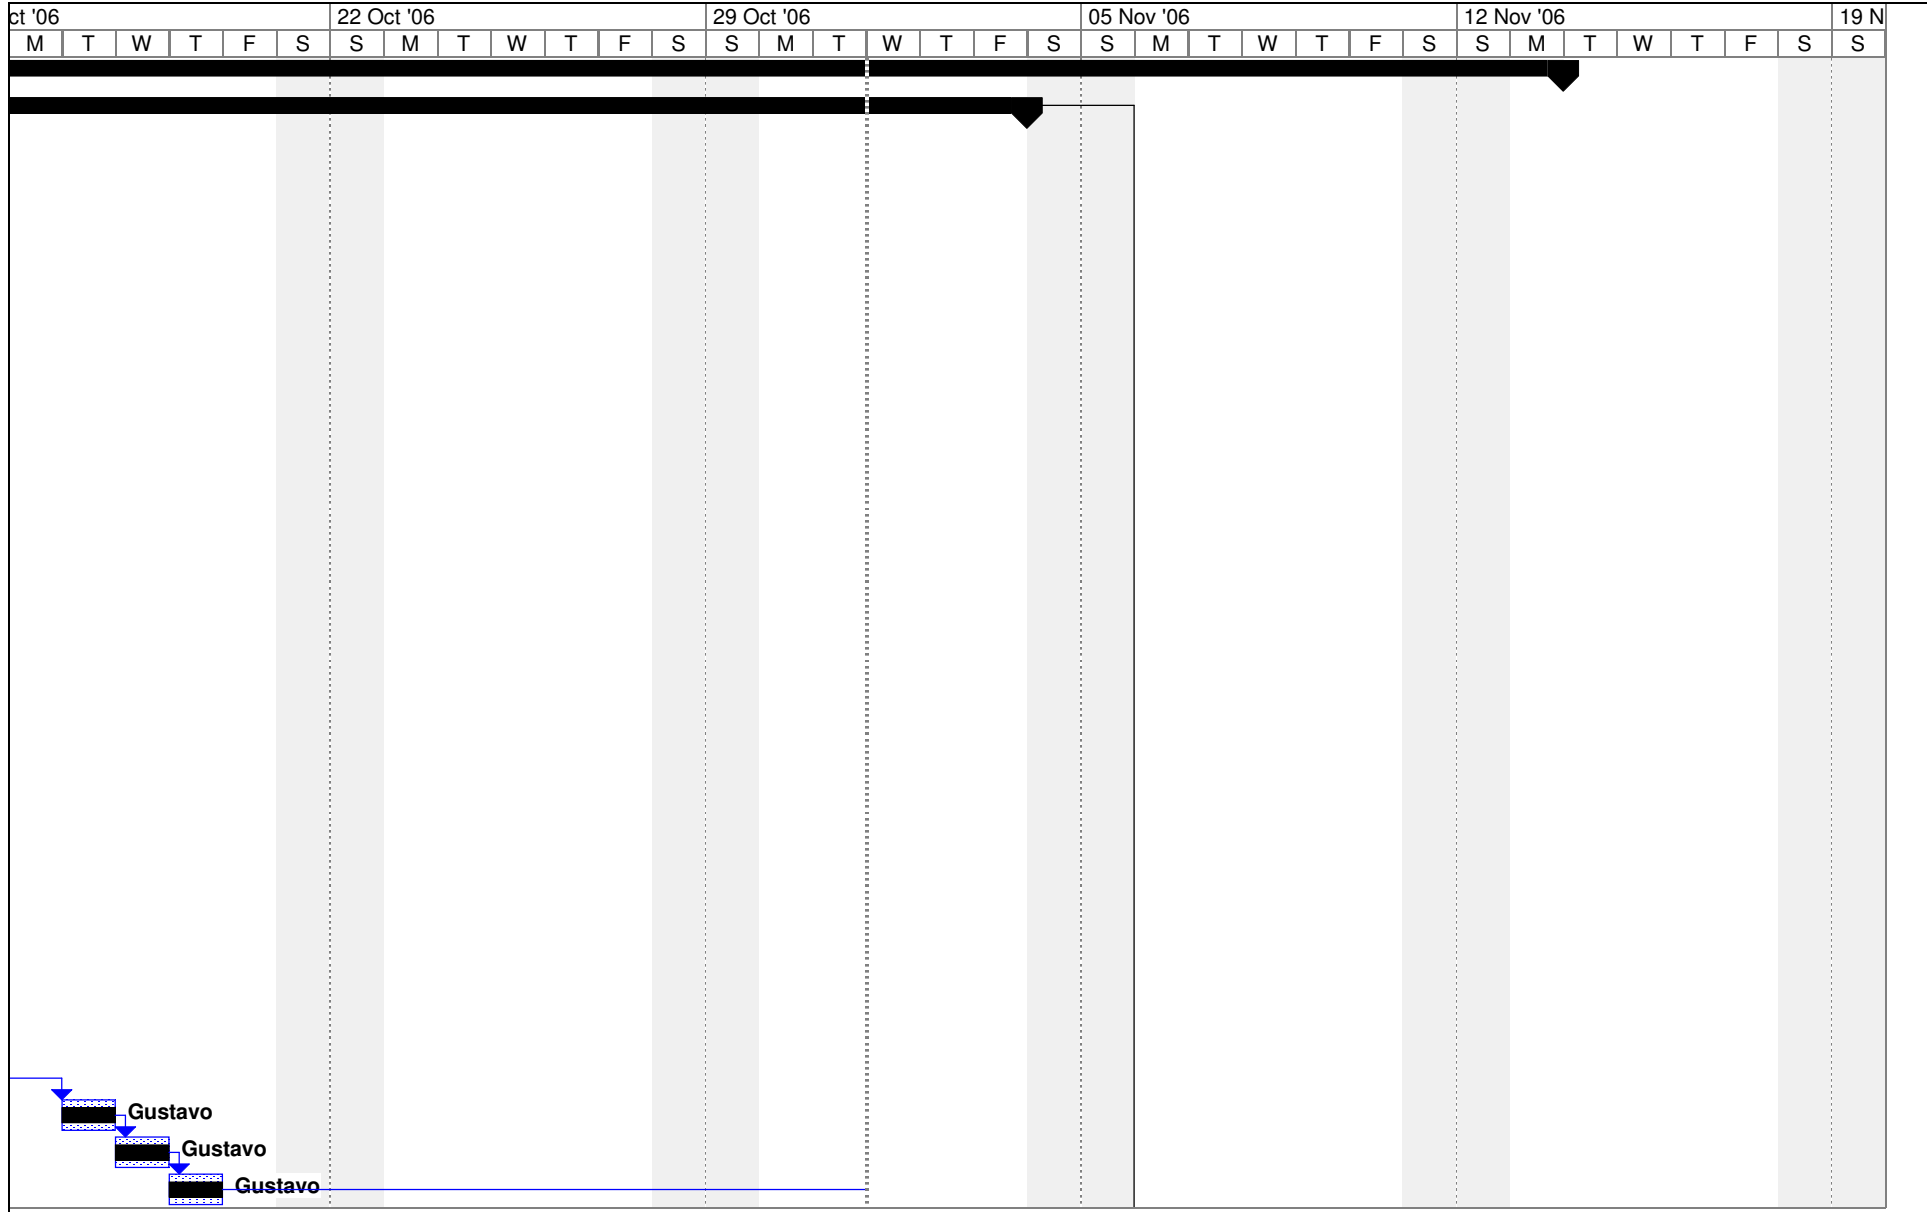


Project: Plan PRs Date: Wed 01/11/06	Task	Milestone	External Tasks
	Split	Summary	External Milestone
	Progress	Project Summary	Deadline



Project: Plan PRs Date: Wed 01/11/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: Plan PRs Date: Wed 01/11/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

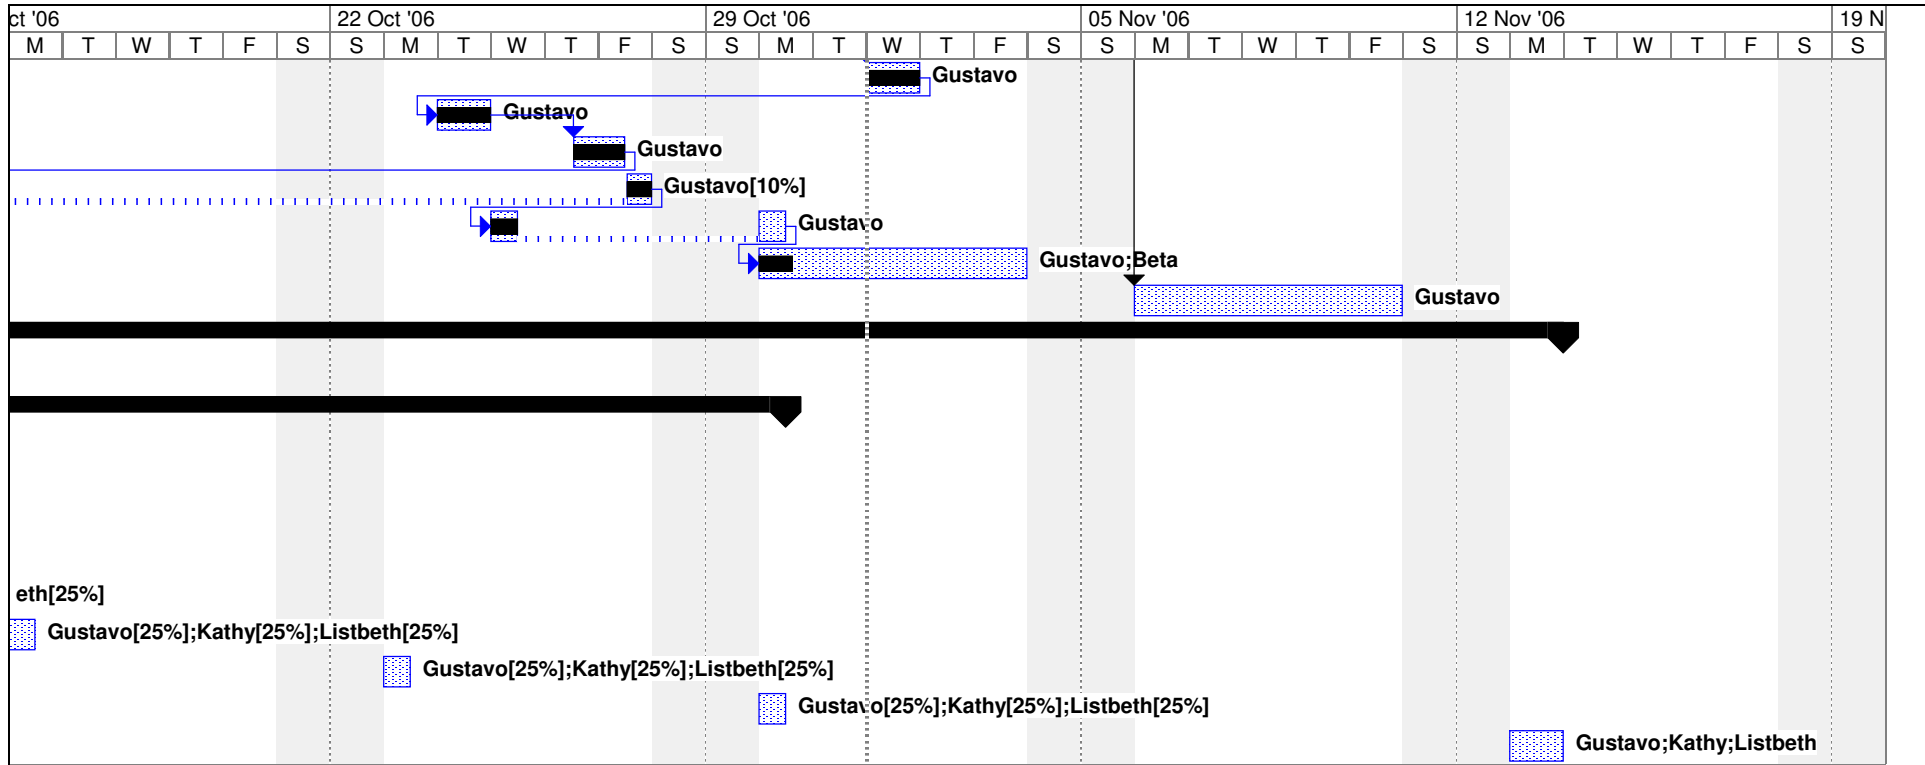

Project: Plan PRs Date: Wed 01/11/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
