

What happened? (activities made since the last follow up)

- * Formal Requirements Specification
- * Requirements reviewed by Tierra and adjusted by GWT.
- * Project Plan
- * Data Model Elaboration
- * N2C and WI3 Configuration.
- * Partial Implementation of the Site's Template
- * Site's Pages Definition

What should have happened? (activities until the follow up date)


- * Total Construction of the Site's Template
- * Testing Plan Elaboration
- * login/logout and password change implementation
- * 75% of the Registration Process Development
- * Public and User Home News/ Dealer News

Areas of attention

- * Delayed Activities (Bring up to date)
- * Final Approval of the Requirements Specifications (send to Arne Postma -Tierra Network- at 13-Nov-2006)

What are the next activities? (Tasks and responsibilities)

- * Home News Implementation. Person in charge: GWT 20 Nov 2006
- * User Registration Implementation. Person in charge: GWT 21 Nov 2006
- * Site's Template and login facilities culmination . Person in charge:GWT 17 Nov 2006
- * Testing Plan Elaboration. Person in charge: GWT 20 Nov 2006
- * Execution of the programmed activities (According to the plan)

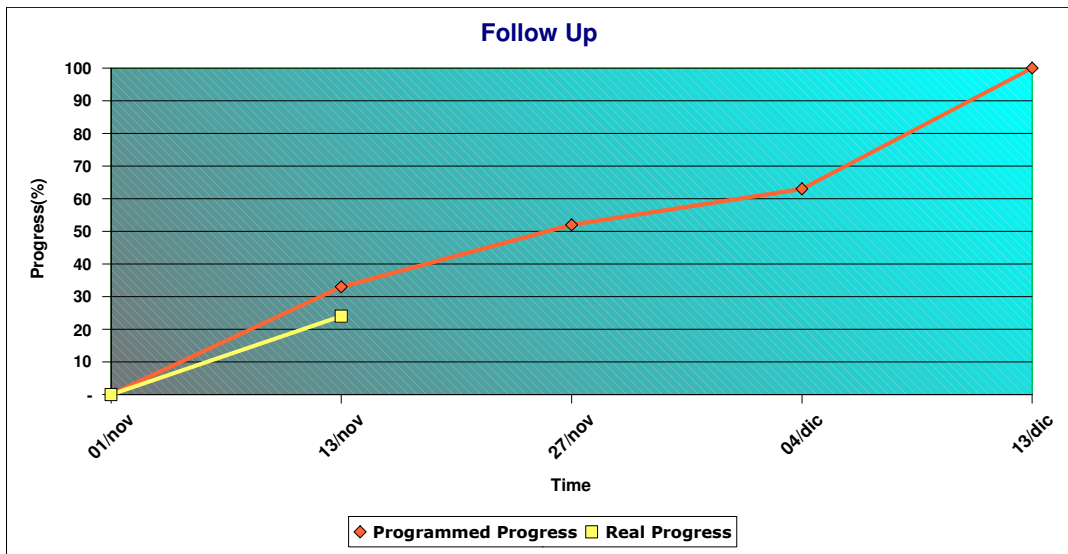

| Date | 1-nov | 13-nov | 27-nov | 4-dic | 13-dic |
|------------|-------|--------|--------|-------|--------|
| Programmed | 0,00 | 33,00 | 52,00 | 63,00 | 100,00 |
| Real | 0,00 | 24,00 | 0,00 | 0,00 | 0,00 |

| Legend | |
|---------------------------------------|-----------------------------------|
| ● | Deviation <= 5% |
| ● | Deviation > 5% y Deviation <= 10% |
| ● | Deviation > 10% |

| Follow Up | Programmed Progress | Real Progress |
|-----------|---------------------|---------------|
| 01/nov | - | - |
| 13/nov | 33,00 | 24,00 |
| 27/nov | 52,00 | |
| 04/dic | 63,00 | |
| 13/dic | 100,00 | |
